



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

6/12/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU shaping North chipping green, coring out South chipping green, hauling old greens mix & gravel to driving range tee, and doing demo on the bunker adjacent South chipping green.

Tuesday - LU shaping North chipping green, coring out South chipping green, and hauling old greens mix & gravel to driving range tee. Dave Taylor staking irrigation on holes #6, 8-13, NCG, and SCG.

Wednesday - LU shaping #8 green, completed coring out #9 green, prepping subgrade of #8 & North chipping greens, and bagain backfilling edges of North chipping green.

Thursday - LU shaping #9 & South chipping green, prepping subgrade of #8 green, backfilling edge of #8 green and irrigation starts fusing 4" HDPE pipe.

Friday - LU finishes shaping #9 green, prepping subgrade of #9 and South chipping green, backfilling edges of #9 and South chipping green. Irrigation fusing HDPE pipe.

Saturday - Crew off.

Total Man Hours for Work Week: Construction = 791 , Irrigation = 80, Total = 871 hours.

Equipment on Site Being Utilized: 3 excavator's, 3 tractor w/ trailers, skid steer, skip loader, and 3 utility carts.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	0



Coring out North chipping green.



Backfilling bunker on South chipping green.



Watering and compacting driving range tee



Coring out South chipping green.



Filling holes in subgrade.



Shaping #9 green.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

7/3/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU coring #1 green, shaping #5 fairway, and installing irrigation greens loop on North CG.

Tuesday - LU coring #6 green, draining #1 green, shaping #5 fairway, installing greensmix on South CG, and installing irrigation greens loop on North CG.

Wednesday - LU coring #6 green, draining #1 green, shaping #5 green complex, installing greensmix on South CG, and installing irrigation heads on North CG.

Thursday - LU coring #6/7 green, draining #2 green, shaping #5 green complex, installing greensmix in #1 green, and installing irrigation greens loop on South CG.

Friday - LU coring #7 green, draining #2 green, shaping #5 green complex, installing greensmix in #1 green, and installing irrigation greens loop on South CG.

Saturday - LU coring #7 green, prepping subgrade on #3/6/7 greens for Kevin, and shaping #5 green complex.

Total Man Hours for Work Week: Construction = 889 , Irrigation = 204, Total = 1,093 hours.

Equipment on Site Being Utilized: 1 dozer, 3 excavators, 4 tractors w/ trailers, 2 dumpers, skid steer, skip loader, 2 PU trucks, and 3 utility carts.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
Lone Mountain Sand Company misses scheduled delivery of greens mix.	4
	0
Days Impacted - Project to Date	4



Stripping #5 green.



New green complex on hole #5.



Coring out #7 green.



Installing drainage and pea gravel on #1 green.



#5 greens cavity.



#5 new approach.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

7/10/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU draining #4 green, making adjustments on #3/6/7 greens, installing greensmix in #2 green, and splicing irrigation connections on South CG.

Tuesday - LU coring out #10 green, making adjustments on #3/6/7 greens, installing greensmix in #2 green, shaping #5 green complex, and fusing 3" & 4" HDPE irrigation pipe for greens loops.

Wednesday - LU coring out #10 green, draining #4 green, shaping #5 green complex, and trenching for 4" HDPE irrigation pipe on #6 green.

Thursday - LU coring out #11 green, draining #4 green, and installing 4" HDPE irrigation pipe for #6 green.

Friday - LU installing greensmix on #4 green, draining #3 green, and installing 4" HDPE irrigation pipe for #6 green.

Saturday - LU doing initial prep of #5 fairway & green complex, and draining #3 green.

Sunday - LU installing greensmix in #3 green.

Total Man Hours for Work Week: Construction = 940, Irrigation = 175, Total = 1,115 hours.

Equipment on Site Being Utilized: 1 dozer, 3 excavators, 4 tractors w/ trailers, 2 dumpers, skid steer, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



Covering North CG with plastic tarp.



Draining #4 green.



Coring out #10 green.



Installing greensmix in #4 green.



Draining #3 green.



Installing greensmix on #2.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

7/17/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU coring out #11 green, shaping #7 bunker, and shaping # 5 fairway.

Tuesday - LU coring out #12 green, draining #6 green, and shaping #5 bunkers.

Wednesday - LU coring out #12 green, draining #6 green, and shaping #5 bunkers.

Thursday - LU Coring out #13 green, draining #6 green, and shaping #5 bunkers.

Friday - LU coring out #13 green, and draining #5 & #7 green.

Saturday - LU coring out #14 green, and draining #5 & #7 green.
installing greensmix into #3 green.

Sunday-

Total Man Hours for Work Week: Construction = 1,226, Irrigation = 22, Total = 1,248 hours.

Equipment on Site Being Utilized: 3 excavator's, 4 tractor w/ trailers, 2 dumpers, skid steer, skip loader, and 4 utility carts.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
Days Impacted - Project to Date	4



Cartpath Demo on #5




Draining #5 green



Covering #2 green with plastic tarp



#13 green cavity

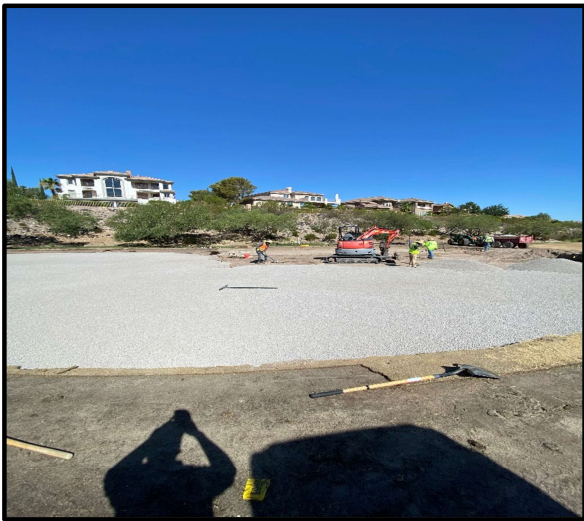

Draining #7 green



Right side bunker on #5 green complex



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

7/24/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU coring out #14 green, installing greensmix in #6 green, floating #4 green, frase mowing #9 fairway and prepping haul roads.

Tuesday - LU coring out #14 green, installing greensmix on #6 & #5 green, floating #3 green, frase mowing #9 & #1 fairway and prepping haul roads.

Wednesday - LU installing greensmix in #5 green, draining #7 & #5 bunkers, floating #3 green, frase mowing #1 & #2 fairway, prepping haul roads, and installing irrigation on #5 fairway.

Thursday - LU installing greensmix in #7 green, draining #5 bunkers, floating #5 green, frase mowing #2 & #3 fairway, prepping haul roads, installing irrigation on #5 fairway.

Friday - LU installing greensmix in #7 green, draining #10 green, floating #5 green, frase mowing #3 & #5 & #6 fairway, prepping haul roads, and installing irrigation on #5 fairway.

Saturday - LU draining #10 green, floating #6 green, prepping #9 fairway and haul roads, frase mowing #7 & #8 fairway, and installing irrigation on #5 green.

Total Man Hours for Work Week: Construction = 1,174, Irrigation = 200, Total = 1,374 hours.

Equipment on Site Being Utilized: 4 excavator's, 6 tractor w/ trailers, 1 tractor w/koro, 2 dumpers, skid steer, skip loader, and 4 utility carts.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
Days Impacted - Project to Date	4



Frase mowing #1 fairway



Draining #10 green



Covering #3 green with plastic tarp



Anthem CC aerifing #9 fairway



Draining #7 bunker



Frase mowing #9 fairway



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

7/31/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU draining #11 green, prepping green collars, fraze mowing on #8 fairway, and installing irrigation pipe on #6.

Tuesday - LU draining #11 green, prepping #9 fairway & green complex, installing irrigation pipe on #6. West Coast Turf installing collar sod on complexes #1,2,3,4,5,8,9, NCG and SCG.

Wednesday - LU draining #12 green, prepping #1 fairway and green complex, shaping driving range tee, and installing irrigation laterals on #5 FWY. WCT installing sod on #9 FWY.

Thursday - LU draining #12 green, prepping #1 fairway, shaping driving range tee, and installing irrigation laterals on #5 FWY. WCT installing fairway sod on #9,1.

Friday - LU shaping bunker on #15 green complex, prepping #2 fairway and green complex, and installing irrigation laterals and setting heads on #5 fairway. WCT installing fairway sod on #1.

Saturday - LU continues shaping bunker on #15, building new tee on #14, prepping #3 fairway and green complex, and installing irrigation laterals and setting heads on #5 fairway. WCT installing fairway sod on #1,3.

Total Man Hours for Work Week: Construction = 990, Irrigation = 448 , Total = 1,438.

Equipment on Site Being Utilized: 4 excavators, 6 tractors w/ trailers, 1 tractor w/ fraze mower, 2 dumpers, skid steer, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



Complex #9 grassed.




Complex #10 gravel layer installed.



Fairway #9 grassed.



South DR tee & SCG in progress.

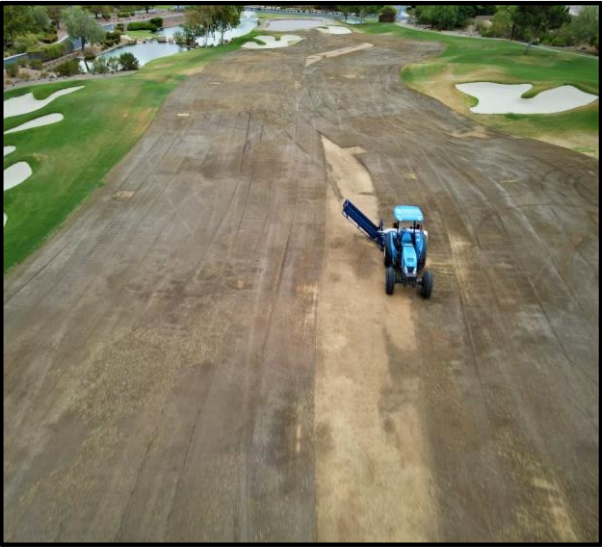

Fraze mowing on #10 fairway in progress.



Shaping #15 bunker.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

8/7/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU starts coring out #15 green, draining #14 green, prepping #3 fairway, and installing 4" irrigation HDPE pipe on #10 green.

Tuesday - LU continues coring out #15 green, draining #14 green, prepping #3,6 fairway, and installing 4" HDPE irrigation pipe on #10 green.

Wednesday - LU starts shaping #15 green, draining #13 green, prepping #5 fairway, shaping driving range tee, and installing 3" HDPE irrigation pipe around #10 green.

Thursday - LU continues shaping #15 green, draining #13 green, prepping #5 fairway, shaping driving range tee, and installing irrigation maxi wire on #5.

Friday - LU starts coring out #16 green, draining #15 bunker, prepping #5 fairway, shaping driving range tee, and trenching irrigation greens loop on #11.

Saturday - LU continues coring #16 green, prepping #5 fairway, shaping driving range tee, and installing 4" HDPE irrigation pipe on #11 green.

Total Man Hours for Work Week: Construction = 1,138, Irrigation = 285 , Total = 1,423.5

Equipment on Site Being Utilized: 4 excavators, 6 tractors w/ trailers, 1 tractor w/koro, 2 dumpers, 2 skid steers, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



Shelley coring out #15 green.



Floating #7 green.



Draining #14 green.



Draining #13 green.



Laser leveling driving range tee.



Prepping #5 fairway.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

8/14/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU cores out #16 green, shaping #15 green, installing capillary concrete on #5 greenside bunkers, prepping #5 fairway, and installing 3" HDPE irrigation pipe around #11 green.

Tuesday - LU starts coring #17 green, shaping #15 green, installing capillary concrete on #7,15 bunker, prepping #5 fairway, and installing 3" HDPE irrigation pipe around #11 green.

Wednesday - LU continues coring out #17 green and starts coring out #18 green, draining #15 green, prepping #5 fairway, and installing 4" HDPE irrigation pipe around #12 green.

Thursday - LU continues coring out #18 green and starts coring out PG, draining #15 green, prepping #5 fairway, and installing 3" HDPE irrigation pipe around #12 green.

Friday - LU continues coring out PG, draining #16 green, prepping #5 fairway, installing bunker sand on #5 greenside bunkers, and installing 4" HDPE irrigation pipe around #13 green.

Saturday - LU continues coring out PG, draining #16 green, prepping #6,7 fairway, and installing 3" HDPE irrigation pipe around #13 green.

Total Man Hours for Work Week: Construction =1,078, Irrigation = 304, Total =1,382

Equipment on Site Being Utilized: 4 excavators, 6 tractors w/ trailers, 1 tractor w/koro, 2 dumpers, 2 skid steers, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



Coring out putting green.



Draining #15 green.



#5 fairway grassed.



Coring out #18 green.



Installing mix in #15 green.



Prepping #6.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

8/28/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU fraze mowing #13,14 fairway, draining #18 green, shaping DR tee, prepping #8 green for seed, and trenching irrigation lines on DR tee.

Tuesday - LU fraze mowing #15 fairway, shaping main PG & DR tee, prepping #6,7 greens for seed, prepping #10 fairway for sod, and installing irrigation heads on DR tee.

Wednesday - LU fraze mowing #16,17 fairway, shaping main PG, prepping #10,11 greens for seed, and installing irrigation heads on DR tee.

Thursday - LU fraze mowing #18 fairway, adjusting sand depths on #13,14 green, prepping #11 fairway for sod, and laser leveling DR tee.

Friday - LU prepping #12 fairway for sod, prepping #13,14 greens for seed, and laser leveling DR tee.

Saturday - LU prepping #13,14 green collars for sod, adjusting sand depths on #15,16 green, and laser leveling DR tee.

Total Man Hours for Work Week = 1,265

Equipment on Site Being Utilized: 3 excavators, 6 tractors w/ trailers, 1 tractor w/ fraze mower, 2 dumpers, 2 skid steer, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



Fraze mowing on #11.



Anthem CC crew seeding #9 green.



Prepping DR tee.



New swale on #8.



New bunker on #5.



Prepping #9 green for seed.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

9/11/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU installing greensmix in putting green and prepping #15 fairway.

Tuesday - LU installing greensmix in putting green and prepping #15 fairway.

Wednesday - LU installing greensmix in putting green and prepping #16 fairway.

Thursday - LU floating putting green and prepping #17 fairway.

Friday - LU floating warm up green on #1 tee complex and prepping #18 fairway.

Saturday - LU prepping #18 fairway and prepping #14 tee.

Total Man Hours for Work Week: Construction = 900, Irrigation = 50 , Total = 950

Equipment on Site Being Utilized: 3 excavators, 6 tractors w/ trailers, skid steer, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



#9 fairway grow in progress.



Installing greensmix in #18 green.



Prepping new tee on #14.



#14 green & fairway grassed.



Putting green being drained.



Driving range tee grassed.



Project Status Report

Project: 2207 Anthem Country Club Greens Rebuild

Dave Linngren - Regional Manager

9/18/2022

Report by Elliot Tagliapietra

Tasks Completed Last Week

Monday - LU completing punchlist items.

Tuesday - LU completing punchlist items.

Wednesday - LU completing punchlist items.

Thursday - LU completing punchlist items.

Friday - LU completing punchlist items.

Saturday - LU completing punchlist items.

Total Man Hours for Work Week: Construction = 900, Irrigation = 50 , Total = 950

Equipment on Site Being Utilized: 1 excavators, 3 tractors w/ trailers, 1 skid steer, skip loader, 4 utility carts, and 2 PU trucks.

Items to Rectify / Address (2+ Week Look-Ahead)

Action by Whom

Weather / Schedule Impacts

Project Days Impacted

Weather forecast ahead looks satisfactory.	0
	0
	0
Days Impacted - Project to Date	4



New chipping area on south chipping green.



#18 fairway grassed.



#12 grassed.



PG grassed.



#17 grassed.



#12 fairway grassed.
